CDC Enterprise Performance Life Cycle

Overall Critical Partner Information

Level of Engagement (LOE)

		Acquisition	Budget/ Finance	Capital Planning	Enterprise Architecture	Human Resources	Infrastructure	Performance	Records Management	Section 508	Security
Initiation	A	H	H	M	H	L	M	M	M	L	L
Concept	B	H	H	M	H	M	H	H	M	M	M
Planning	C	H	H	H	M	H	M	M	M	H	H
Requirements Analysis	D	M	M	H	H	M	M	M	M	M	H
Design	E	M	M	L	H	L	L	M	M	H	M
Development	F	L	M	L	L	L	L	M	H	M	L
Test	G	L	M	L	L	L	L	M	M	L	H
Implementation	H	L	H	M	L	M	L	L	M	L	M
Operations & Maintenance	I	M	L	H	H	L	M	L	H	H	M
Disposition	J	L	M	L	L	L	M	L	H	L	M

Generally, the CPIC Critical Partner serves as the lead critical partner

Two Levels of Critical Partners

Enterprise Level

1. Provides leadership and guidance to CIO Critical Partners to ensure consistency across CDC
2. Provides consultation on specific projects as needed
3. Maintains Critical Partner Manuals and other job-aids
4. Provide training to CIO Critical Partners
5. Acts as the local critical partner if needed

CIO Level

1. Participates in all phases and activities of a project including project planning and execution
2. Participates in Project Reviews as appropriate to their respective areas
3. Provides recommendations to the IR Governance body conducting Stage Gate Reviews

Learn Who these Critical Partners Are?

Visit EITPO SharePoint

http://esp.cdc.gov/sites/ocoo/EITPO/EPLC/Pages/cp.aspx

Frequently Asked Questions

Does every critical partner need to participate in every phase?
That depends upon the project. Use the table above to help determine what level of engagement is needed for your project given the risks, complexity, size and mission criticality.

Who decides the critical partner level of engagement?
The project team in consultation with all critical partners (AKA the integrated project team)should make this determination during the completion of the project process agreement, which is approved by CIO IR Governance.

What should I do if one of my critical partner can't participate?
There should be a plan within your CIO on how to handle situations where an individual critical partner is not available to provide the advice and council to the project team. In the event that no one is available, reach out to the enterprise critical partner for assistance.

Special Note

This critical partner job-aid is provided as a summary of the information contain in the full critical partner manuals. As questions arise, please use the complete manuals for all of the perspectives and requirements. Complete versions are found on the EITPO SharePoint Site

http://esp.cdc.gov/sites/ocoo/EITPO/EPLC/Pages/cp.aspx

Overall Critical Partner Responsibilities

Acquisition Management

•To ensure acquisition and project plans adhere to the Federal Acquisition Regulation, HHS Department and CDC acquisition policies and procedures, and successful business practices

Budget & Finance

•To ensure that adequate financial resources have been identified and is available and that there is a realistic budget to accomplish planned work
•To ensure the project's financial needs are adequately identified and planned
•To ensure any of the project's financial management components interact with financial systems in such a way as to ensure compliance with financial standards and regulations

Capital Planning & Investment Control

•To review IT business case and project deliverables to ensure compliance with CPIC policies and procedures
•To provide guidance to project managers regarding the overall project management requirements of EPLC and CPIC
•To coordinate other Critical Partners in the preparation and review during Stage Gates

Enterprise Architecture

•To ensure that IT projects provide demonstrable alignment with the organization's mission, CDC architecture principles, business processes, and technical architecture

Human Resources (May be the Business Owner)

•To ensure the project has the skills and competencies necessary to accomplish the business objectives
•To ensure human resource and union issues that may affect a project's progress are addressed in an appropriate manner

IT Infrastructure

•To ensure that an IT project provides demonstrable alignment with CDC IT infrastructure, services, facilities, and processes

Performance (May be the Business Owner)

•To identify the business needs and the performance measures to be satisfied by their projects
•To ensure their projects achieve the mission, strategic and operational business needs of CDC while meeting the business need
•To provide the overall financial and management responsibility

Records Management

•To provide guidance to project managers on Records Management requirements
•To ensure that the project schedule and budget address Records Management needs, such as retrieval, storage, and disposition
•To ensure that projects adhere to Records Management policies and procedures

Section 508

•To ensure the project design and any associated contracts contain all of the accessibility requirements
•To ensure issues related to accessibility are identified and addressed prior to implementation

Security

•To ensure projects demonstrate that the appropriate planning and budgeting for the appropriate IT privacy and security controls are explicitly incorporated into the life cycle
•To ensure if requirements reflect alignment with established information security standards including FIPS-199 Categorization and Accreditation Boundary
•Determine if Plan of Objectives & Milestones and Authority to Operate are complete

Based on EPLC Version 2.0

CDC Enterprise Performance Life Cycle
Acquisition Critical Partner Information

	LOE	Top Major Probing Questions For Consideration	Top Risks
Initiation	H	Does the organization have the existing skills to carry out this project, or where will the project look to obtain them? What issues and/or risks from your perspective do you see that would affect the development of a business case?	Identify potential risks, impacts, events, causes, and potential consequences associated with Project Initiation Phase HHS AP
Concept	H	How does the Business Case address a performance-based Acquisition Strategy, and how adequately does it meet the requirements definition?	Identify add-in potential risks, impacts, events, causes, and potential consequences associated with Project HHS AP
Planning	H	How well have acquisition activities to obtain contractor support been completed, and how have they maintained compliance with the Project Management Plan?	Identify add-in potential risks, impacts, events, causes, and potential consequences associated with Project HHS AP
Requirements Analysis	M	How adequately does the acquisition strategy include necessary requirements analysis, alternatives analysis, and procurement and contract award plans?	Identify add-in potential risks, impacts, events, causes, and potential consequences associated with Project HHS AP
Design	M	What, if any, changes in the high-level architectural design introduce the need to modify the overall Acquisition Plan or Task Order?	Identify add-in potential risks, impacts, events, causes, and potential consequences associated with Project HHS AP
Development	L	How strictly are all contracts being performed according to award requirements or approved changes? Have required assets (e.g., system hardware, COTS/GOTS software) been acquired according to regulations?	Identify add-in potential risks, impacts, events, causes, and potential consequences associated with Project HHS AP
Test	L	What, if any, changes have resulted in contract modifications, and how have they been reviewed?	Identify add-in potential risks, impacts, events, causes, and potential consequences associated with Project HHS AP
Implementation	L	Which, if any, approved change requests for the project require modification in cost, schedule, scope, or resources? Have the necessary infrastructure and associated products for the production environment been acquired, configured, and integrated?	Identify add-in potential risks, impacts, events, causes, and potential consequences associated with Project HHS AP
Operations & Maintenance	M	What is the status of all contracts, and have they been performed and closed out?	Identify add-in potential risks, impacts, events, causes, and potential consequences associated with Project HHS AP
Disposition	L	Who has verified that all completed contracts have been closed appropriately?	Identify add-in potential risks, impacts, events, causes, and potential consequences associated with Project HHS AP

Approved by the relevant Enterprise Critical Partner as a synopsis of the information contained in the full CPIC Critical Partner Manual

Based on EPLC Version 2.0

CDC Enterprise Performance Life Cycle

Budget/Finance Critical Partner Information

	LOE	Top Major Probing Questions For Consideration	Top Risks
Initiation	H	Given the rough order of magnitude (ROM) estimates, what actions will the business owner need to take to prepare and communicate so that the budget will be sufficient to meet the needs of the project completion?	Lack of communicating expected costs for each phase to stakeholders, finance office, etc.
Concept	H	What, if any, issues and/or risks from your perspective do you see that would affect the development of a business case? How adequately are the financing and budgeting plans covered in the Business Case?	Not adequately assessing the potential costs both for the development and operations & maintenance
Planning	H	Does the budget account for the Total Cost of Ownership(TCO)? What is the status of funding and how much funding has been allocated to the project? How realistic is the budget to accomplish all planned work, and how does it account for the TCO?	Mechanisms have not been identified to handle any cost and schedule variances
Requirements Analysis	M	What are the financial management requirements, and how are they in accordance with requirements established at the end of the Planning Phase? How well do the cost baselines match the requirements established at the Planning Phase?	Obligation of funds prior to clear, approved requirements that meet the scope of the effort
Design	M	Given the current design, what changes in the budget will be required to meet the needs of the project? Given the high-level architectural design, what additional risks have been considered and planned for?	Expected benefits and business outcomes are not realized
Development	M	What are actual expenses and how do they track to the budget plan? What shortfalls or variances are there in the budget, and how sufficiently is the budget meeting the needs of the project?	Expected benefits and business outcomes are not realized
Test	M	What is the financial impact of any planned changes? How sufficient is the budget continuing to be at meeting the needs of the project?	Mitigation plan does not sufficiently identify the potential problems that affect cost or outcome of the project
Implementation	H	Which, if any, approved change requests for the project require modification in cost, schedule, scope, or resources? Given results of the Test Phase and the Implementation Readiness Review, System Certification, and System Accreditation, how sufficient will the budget be in meeting the needs of the project completion?	Operational costs are not adequately defined separate from or in addition to project costs
Operations & Maintenance	L	What was the actual project cost compared to plan? What is the status of all final bills/receipts, and are they complete? What was the outcome of the current cost benefit analysis?	All resources or organizations supporting the solution are not realizing actual costs via implementation of SLA's or MOU's
Disposition	M	Who has verified that all final payments to contractors have been made? How accurately have all project financial information/status been updated? Who has reviewed the financial implications of the disposition/transition for budget impacts?	Loss of financial information if not properly disposed of or archived

Approved by the relevant Enterprise Critical Partner as a synopsis of the information contained in the full CPIC Critical Partner Manual

Based on EPLC Version 2.0

CDC Enterprise Performance Life Cycle

Capital Planning & Investment Control (CPIC) Critical Partner Information

	LOE	Top Major Probing Questions For Consideration	Top Risks
Initiation	M	Does the Business Needs Statement indicate the anticipated Cost and Benefits?	Business Needs Statement incomplete
Concept	M	What was the basis for choosing the Alternative you are planning to use? Does the Project Plan include a complete Budget Estimate and schedule for the Project? Has the IT Activity been entered in the Enterprise System Catalog(ESC)?	Duplicate or redundant systems
Planning	H	Does the Project Plan include a complete Budget Estimate and schedule for the Project?	Unrealistic Budget estimates Schedule has no room for unexpected events
Requirements Analysis	H	Does the Requirements document include resource plan for both FTE and Contractor? Does the Requirements Document indicate the stakeholders for the Project? Are the baselines established and the process for tracking and reporting against that baseline?	Stakeholders not identified Not enough resources are available to meet requirments
Design	L	Does the design meet the needs as outlined in the Business Needs and Requirement documents? Are risks being tracked and mitigation plans being followed?	Overly complex design solution that lead to issues with implementation and ongoing maintenance
Development	L	Has the C&A been granted or when is it planned?	Significant issues causing project schedule to slip and budget overruns
Test	L	Has the system been documented and modeled in CDC's repositories – HEAR, ESC?	Improper or inadequate testing negatively affects the quality and efficiency of the system
Implementation	M	Has an ATO for the System been granted? What are the established plans for reporting cost and schedule? Is the Project meeting the Estimated Budget?	Security issues uncovered too late Funding not available to move the project forward
Operations & Maintenance	H	Does the product still meet outcomes and expected results? Have you conducted a complete Operational Analysis? Is the system delivering expected business objectives	Not meeting expected outcomes or needs New Project has to be started to overcome deficiencies
Disposition	L	Has the IT activity been given final disposition by Security? Has the It activity been retired from ESC?	Replacement IT activity not available on time to complete disposition

Approved by the relevant Enterprise Critical Partner as a synopsis of the information contained in the full CPIC Critical Partner Manual

Based on EPLC Version 2.0

CDC Enterprise Performance Life Cycle

Enterprise Architecture (EA) Critical Partner Information

	LOE	Top Major Probing Questions For Consideration	Top Risks
Initiation	H	Are there any overlapping or redundant systems that offer similar functionality? Is the new business need common across other organizations?	Duplicate or redundant systems that are poorly aligned to the strategy result in less than effective use of IT dollars
Concept	H	Are there any overlapping or redundant systems that offer similar functionality? Is the high level solution concept sufficiently described?	Insufficient description of the conceptual solution impacts stakeholder expectations, schedule, and cost estimates
Planning	M	Are collaboration activities with other organizations appropriately planned? Does the Project Plan account for building and/or leveraging shared services?	Plans do not appropriately reflect the creation of key artifacts as well as collaboration with cross-organization teams
Requirements Analysis	H	How complete are the critical documents such as process models, data flows, and requirements? Have the relevant technical standards and vocabulary been identified?	Performance gaps due to insufficiently detailed architecture models and requirements
Design	H	Is the design leveraging existing architecture blueprints, principles, and standards? What standards are used in the design of the system that advances interoperability with other systems (e.g. NIEM, HL-7, ICD-10, etc.)?	Overly complex design solution that leads to issues with implementation and ongoing maintenance
Development	L	Was the minimum required technical documentation updated and made available as changes occurred during Development?	Changes made during development move the solution away from the agreed upon design and this could mean lost benefits
Test	L	Were the test plan, types of tests, and results adequate for this solution?	Improper or inadequate testing negatively affects the quality and efficiency of the system and enabled business processes
Implementation	L	Was the technical documentation updated and made available as changes occurred during test and implementation?	Changes made during test and last minute configurations are not reflected in documentation contribute to increased O&M costs
Operations & Maintenance	H	Does the product still meet outcomes and expected results? Does it remain aligned with relevant and current Architecture References?	Modifications to large systems are more difficult and costly than changes to loosely coupled, modular service components
Disposition	L	Have dependencies and relationships to the expired system been redirected, or expired?	Failure to fully plan for a systems retirement can result in serious disruptions especially with dependent systems

Approved by the relevant Enterprise Critical Partner as a synopsis of the information contained in the full CPIC Critical Partner Manual

Based on EPLC Version 2.0

CDC Enterprise Performance Life Cycle
Human Resources (HR) Critical Partner Information

	LOE	Top Major Probing Questions For Consideration	Top Risks
Initiation	L	Has a business owner and/or sponsors been identified?	Without an appropriate business owner, project runs the risk of failing and not being carried out fully
Concept	M	Does the business owner have the appropriate competencies and skillsets to carry out the project? Has a project manager been identified along with other members of the team?	Without the appropriate level of expertise and competencies, project could be impacted
Planning	H	Does the plan include identifying subject matter experts to participate in the requirements analysis phase? Has appropriate staff development issues been addressed in the plan? Does the plan include requirements to conduct current state analysis and future state analysis?	Implementing a project without addressing the workforce implications will result in failure of the project
Requirements Analysis	M	Does the plan address conducting fit gap sessions including identifying SMEs to participate? Do the process models require changes in business processes impacting the workforce? Have the number and types of impacted workforce been identified?	Implementing a project without addressing the workforce implications will result in failure of the project
Design	L	Given the high-level architectural design, is the project staffing sufficient to meet the needs of the project to completion?	Implementing a project without addressing the workforce implications will result in failure of the project
Development	L	How have issues related to staffing, workforce, or other HR areas been addressed	Implementing a project without addressing the workforce implications will result in failure of the project
Test	L	What, if any, issues have been addressed related to staffing, workforce, or other HR areas?	Implementing a project without addressing the workforce implications will result in failure of the project
Implementation	M	Given results of the Test Phase and the Implementation Readiness Review, System Certification, and System Accreditation, how sufficient is the project staffing to meet the needs of the project to completion?	Implementing a project without addressing the workforce implications will result in failure of the project
Operations & Maintenance	L	How well have "lessons learned" about staffing, workforce, or other HR areas been collected and documented? What issues and/or risks do you see that would affect the disposition of this project?	Implementing a project without addressing the workforce implications will result in failure of the project
Disposition	L	Where is all the documentation archived, and is it complete? Has all workforce information been updated, and have staff re-assignments been executed?	Not addressing the staff implications for those no longer needed to sustain a system can result in displaced employees/staff

Approved by the relevant Enterprise Critical Partner as a synopsis of the information contained in the full CPIC Critical Partner Manual

Based on EPLC Version 2.0

CDC Enterprise Performance Life Cycle

Infrastructure Critical Partner Information

	LOE	Top Major Probing Questions For Consideration	Top Risks
Initiation	M	What is the scope and scale of the business need?	Assumptions about infrastructure availability and suitability becoming embedded within the project
Concept	H	Does this initiative potentially depend on an IT Service or Infrastructure Component that is not currently available in the existing IT Service Portfolio? Alternative Analysis - Is this initiative a potential candidate for deployment as a Cloud-hosted service?	Under or over-estimating the business, technical and security requirements and associated levels of effort
Planning	M	Has the scope of the initiative changed since initiation? Have processes, procedures, and standards related to IT governance and IT infrastructure operations been considered?	Mismatch between system design assumptions and CDC IT processes and/or services
Requirements Analysis	M	What are the requirements for network, hardware, database, and supporting software interoperability? Does the initiative call for High Availability, Fault Tolerance, or related capabilities? What are the recovery and restoration requirements, based on business impact and risk?	Mismatch between system functional requirements and CDC IT processes and/or service
Design	L	Where appropriate, has sanitized data been generated for use in the Dev/Test environment? Have change control procedures related to configuration, patches, updates, fixes, and any changes been approved by the project team?	Changes made during system design do not take into account CDC IT processes and/or services
Development	L	Does the current system and IT infrastructure support the projected requirements? Were the information system and IT infrastructure components designed to support both anticipated and unanticipated growth?	Mismatch between as-designed and as-built system which impacts performance, availability and/or cost
Test	L	Has the system's technical steward tested all software-related components? Has the system's developer tested functionality and data elements? Was there any tuning of system or infrastructure configuration issues based on the test results?	Planned and actual resource requirements do not match
Implementation	L	Are all individual system and infrastructure components installed, configured and ready for deployment? Has the impact of changed or updated configuration items been assessed? Has a final review been performed following any required system tuning?	Planned and actual resource requirements do not match
Operations & Maintenance	M	Is there a procedure in place to stay current with vendor patches and updates? Is there a procedure in place to handle high priority/out-of-band patches?	Potential opportunity costs associated with a lack of ongoing review (Cloud Alternative Analysis)
Disposition	M	If the legacy system is being replaced, does the new system and IT infrastructure support all essential business or scientific functions? Have all decommissioning IT Infrastructure related activities been communicated as needed?	"Orphaned" IT resources create unnecessary costs and potential security risks

Approved by the relevant Enterprise Critical Partner as a synopsis of the information contained in the full CPIC Critical Partner Manual

Based on EPLC Version 2.0

CDC Enterprise Performance Life Cycle

Performance Critical Partner Information

	LOE	Top Major Probing Questions For Consideration	Top Risks
Initiation	M	Is this sytem duplicating an already existing system? Are the benefits of the project clearly defined and measurable? Does the initial project scope adequatley address requirements from the business needs statement?	Benefits of the project not identified or measurable Business owner cannot determine funding
Concept	H	Does the organization have existing skills to carry out this project, or where will the project look to obtain them? Has an alternatives analysis been conducted?	Non-quantifiable performance measures, insufficient detail in the business needs & inaccurate as-is and to-be process models
Planning	M	Does the budget account for the Total Cost of Ownership? What is the status of funding and is the project sufficiently staffed? Have performance measures been developed?	Inaccurate/unrealistic time estimates, inaccurate costs calculated, total cost of wonership not defined
Requirements Analysis	M	Do the requirements address all business needs? If needed, what formal changes to the Project Baselines have been requested? Is the project planned, adequately staffed and progressing sufficiently to obtain the end results?	Negative performance impact of changes, and incomplete set of requirements
Design	M	Will any components of the design increase processing time? Does the design meet all required business needs? Is the project sufficiently staffed and proceeding to meet the needs o fthe project to completion?	Not considering performance during design Missing requirements in design
Development	M	Do test plans adequately involve end users and subject matter experts? Are all requirements addressed in development? Are objective milestones that track the project's progress between stage gate reviews being achieved?	Missing requirements in development Negative system impact due to coding approach
Test	M	Have all requirements been verified as being addressed in design and development? How well do the validation tests confirm the business needs were addressed? Is the system functionality perfforming as stated, and is the system able to achieve performance goals?	Insufficient performance testing Not testing full application after making changes
Implementation	L	Have any additional system changes been identified and documented? Given results of the Test Phase and the Implementation Readiness Review, System Certification, and System Accreditation, what additional risks have been considered and planned for?	Customers not aware of and trained on the application changes Support units not aware of support needs
Operations & Maintenance	L	What was the actual project cost compared to plan? What was the outcome of the current cost benefit analysis? How well were service level objectives met and performance measurements and system logs maintained?	Potential difficulty in making agile/timely changes due to business process changes
Disposition	L	Are all financial transactions complete? Where is all the documentation archived, and is it complete?	Failure to identify impact to other systems of system retirement

Approved by the relevant Enterprise Critical Partner as a synopsis of the information contained in the full CPIC Critical Partner Manual

Based on EPLC Version 2.0

CDC Enterprise Performance Life Cycle
Records Management Critical Partner Information

	LOE	Top Major Probing Questions For Consideration	Top Risks
Initiation	M	What type of information/data would be required to meet the Business Need? Does the new business need replace either a manual or automated system? Are there any mandates, legal or otherwise, related to this system data?	Duplication of data, efforts, and costs
Concept	M	Does the high level estimate of cost include Records Management activities such as disposition, destruction, retrieval, and development of a file plan? Does this system replace another system? Is so, has legacy data been considered for inclusion in new system?	Miscalculation of financial and human resources commitments
Planning	M	Have the vulnerabilities of non-conformance to Records Management standards been identified and communicated to individual Program Managers? Have Senior Records Liaisons, Business Stewards, subject matter experts been notified?	Lack of compliance with regulations and CDC/HHS policies
Requirements Analysis	M	Is the Business Owner aware of his/her role in Records Management? Have all Records Management requirements been identified and agreed upon?	Increase costs for managing records Possible loss of data
Design	M	Have strategies been identified for capturing electronic records at every interface between components through which the relevant data passes? Have you determined what metadata to associate with the records?	Records management standards are not implemented
Development	H	Does the development address a migration/integration plan for legacy data? Is Records Management addressed in the Operations & Maintenance manual? Has there been a Data Management Plan developed that includes Records Management?	Records management standards are not implemented
Test	M	Have all Records Management requirements been tested with successful results? Have Records Management monitoring mechanisms been tested with successful results? Has the change management process addressed and accounted for all Records Management issues?	Non-compliance with regulations and CDC/HHS policies
Implementation	M	Has formal documentation of Records Management procedures been included in the Operations & Maintenance Manual? Have all required agreement(s) addressing Records Management been fully executed and implemented?	Lack of consistency in managing active and inactive data
Operations & Maintenance	H	If the Annual Operation Analysis indicates a need to retire the system, is there a well-developed Disposition Plan that includes Records Management requirements? Is the data management plan being followed for the disposition of records?	Non-compliance with regulations and CDC/HHS policies
Disposition	H	Does the Disposition Plan include methods for the deliberate and systematic decommissioning of the system with appropriate consideration of Records Management? Are contracts containing Records Management language, closed?	Data is migrated to format not recognized by NARA

Approved by the relevant Enterprise Critical Partner as a synopsis of the information contained in the full CPIC Critical Partner Manual

Based on EPLC Version 2.0

CDC Enterprise Performance Life Cycle

Section 508 Critical Partner Information

	LOE	Top Major Probing Questions For Consideration	Top Risks
Initiation	L	Has the Business Needs Statement been reviewed by Section 508 staff and key Stakeholders? What, if anything, in the Business Need statement raises concern about conflict with Section 508 standards?	A technology that has known accessibility challenges may be outlined as a business need
Concept	M	Does the Business Case document project include audiences with unique or significant accessibility needs? Is accessibility/508 compliance part of the non-functional requirements?	Choosing an architecture that could increase Section 508 compliance costs and challenges
Planning	H	How completely have the Section 508 compliance requirements been documented in the Project Management Plan components? What plans are in place to incorporate Section 508 requirements and standards in the contract(s)?	Section 508 may not be part of the project requirements or risks
Requirements Analysis	M	Has Section 508 been added to the requirements and risks for the Project? Is the requirement to be 508 compliant understood and documented?	Not including Section 508 compliance in the RTM or risk profile, requiring costly or disruptive remediation activities
Design	H	Have all applicable section 508 requirements identified in the requirements document been incorporated into the system design?	Overly complex systems (solutions) architectures can lead to implementation problems and a higher probability of failure
Development	M	Have section 508 compliance testing been incorporated into the test plans? How adequately are requirements identified for Section 508 compliance incorporated into the system?	Acceptance may not include Section 508, requiring additional costs for accessibility validatio
Test	M	How well do the test plan results meet Section 508 testing requirements? Are the recommended tools being used appropriately? Are the test plan results for testing Section 508 satisfactory?	Changes can lead to "scope creep" and a gradual move away from the agreed upon architecture
Implementation	L	Have the developers followed the checklists and guidance at http://intranet.cdc.gov/508? Have all appropriate Section 508 artifacts been considered?	Changes can lead to "scope creep" and a gradual move away from the agreed upon architecture
Operations & Maintenance	H	Has an alternatives analysis reviewed existing systems for duplicate investments? Is this an opportunity for collaborative development, or adoption of existing Public Health solutions?	Business Needs being supported by the system may change frequently and, sometimes, significantly
Disposition	L	Where is all the documentation archived, and is it complete?	Failure to properly plan for the migration to a new system can result in data collection or data integrity issues.

Approved by the relevant Enterprise Critical Partner as a synopsis of the information contained in the full CPIC Critical Partner Manual

Based on EPLC Version 2.0

CDC Enterprise Performance Life Cycle

Security Critical Partner Information

	LOE	Top Major Probing Questions For Consideration	Top Risks
Initiation	L	What are the potential information security concerns that are raised by the project? What, if any, issues and/or risks from your perspective do you see that would affect the development of a business case?	Underestimating security protections due to unclear business needs and the relation to the data processed within the system
Concept	M	How was the project categorized according to FIPS-199? How have the applicable information security and privacy standards been addressed in the Business Case?	Failure to consider security requirements early
Planning	H	What information security and privacy requirements have been identified, planned for and included in the Project Management Plan? How completely have the Project Management Plan components been developed?	Duplicating existing Enterprise Common Security Control protections already available to meet business needs
Requirements Analysis	H	How thoroughly has the assessment of the required information security controls been completed? How do they reflect alignment with established information security standards, including the FIPS-199 Categorization and Authorization Boundary?	Failing to provide adequate security protections as required by Federal law
Design	M	How closely does the high-level architectural design conform to CDC information security requirements? How completely does the Requirements Traceability Matrix describe how the system design will satisfy the functional, business, information security, and technical specifications in the Requirements Document?	Failing to maintain acceptable risk in regards to the management of a Federal system
Development	L	Has the system been documented and modeled in the HHS EA Repository (HEAR), CDC's ProSight (PMT/OMB 300), Automated Security Authorization Tool, Enterprise Systems Catalog (ESC) and HI.net? How well do all development plans address safety, information security, and privacy concerns?	Losing synchronization with the designed security protections of systems vs. the actual development of the system.
Test	H	How well do the validation tests confirm the information security of the Business Product? What is the result of penetration tests and vulnerability scans, and what is the status any failed components that have been reworked?	Failing to keep management informed of security-related information associated with the test of a system
Implementation	M	What is the status of the System Security Authorization Project Reviews, and how have all issues been resolved? What is the status of the Authorization (to operate) and the System of Record Notice?	Failing to maintain acceptable risk in regards to the management of a Federal system
Operations & Maintenance	M	What is the approval date and approved time period of the Authorization (to operate)? Are there any outstanding items in the plan of action and milestones?	Implementing changes to the system which introduce risk at unacceptable levels Failing to correct security issues timely
Disposition	M	How complete is the documented disposal/transition plan for closing or transitioning the system or its information? Where is the index of preserved information, including its location and retention attributes?	Losing official records should record information not be retained under applicable federal record retention requirements

Approved by the relevant Enterprise Critical Partner as a synopsis of the information contained in the full CPIC Critical Partner Manual

Based on EPLC Version 2.0

CDC Implementation of the
HHS Enterprise Performance Life Cycle

Initiation	Concept	Planning	Requirements Analysis	Design	Development	Test	Implementation	Operations & Maintenance	Disposition

STAGE GATE REVIEWS

- A
- B — Project Selection Review
- C — Project Baseline Review
- D
- E — Preliminary Design Review
- F
- G
- H — Operational Readiness Review
- I
- J

PROJECT REVIEWS

- Architecture Review
- Integrated Baseline Review
- Requirements Review
- Detailed Design Review
- Validation Readiness Review
- Independent Verification & Validation Assessment
- Implementation Readiness Review
- Security Control Assessment
- System Accreditation
- Post-Implementation Review
- Security Authorization
- Annual Operational Analysis

DELIVERABLES

- F Business Needs Statement
- F Business Case
- F Project Charter
- P Project Management Plan
- P Privacy Impact Assessment
- F Project Management Plan
- F Project Process Agreement
- F Requirements Document
- F Design Document
- F Computer Match Agreement
- FD Test Plan
- FD Contingency / Disaster Recovery Plan
- FD System of Record Notice
- F Test Plan
- FD Business Product
- FD O&M Manual
- FD Systems Security Plan
- FD Security Risk Assessment
- FD Training Plan
- FD Training Materials
- FD User Manual
- F Implementation Plan
- F Test Reports
- F Authority to Operate
- F System of Record Notice
- F Business Product
- F Project Completion Report
- F SLAs / MOUs
- F Contingency / Disaster Recovery Plan
- F O&M Manual
- F Systems Security Plan
- F Security Risk Assessment
- F Training Plan
- F Training Materials
- F User Manual
- F Privacy Impact Assessment
- F POA&M
- F Annual Operational Analysis
- F Disposition Plan
- F Continued Authority to Operate
- F POA&M
- F Project Archives

Non-Phase-Specific Deliverables Include:

- Updated Project Management Plan and Schedule
- Earned Value Management Data
- Acquisition Activities / Deliverables
- Periodic Project Status Reports
- Data Use Agreement
- Meeting Minutes

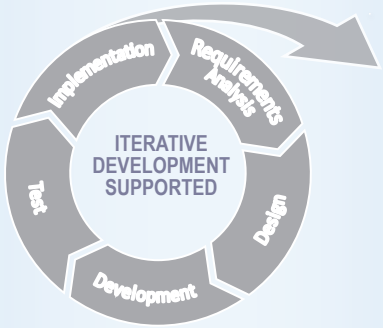

STAGE GATE REVIEWS LEGEND

- ◆ Must be performed by IT governance organization
- ▲ May be delegated

DELIVERABLES LEGEND

- P Preliminary
- FD Final Draft
- F Final

version 2.0
